




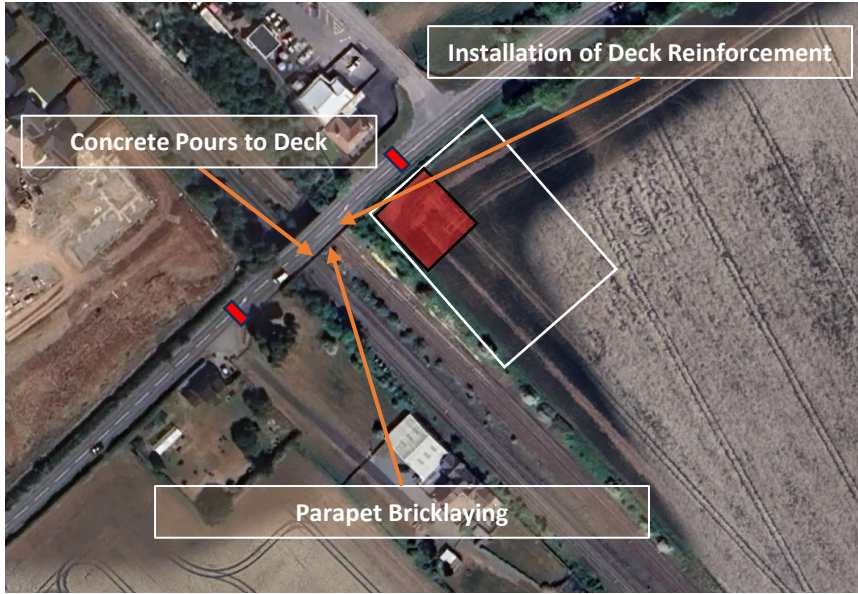

## Four Week Look Back:

Over the past month we have completed the following works, annotated on the image below.

2025				2026						
Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul



Activity	Completion Date	Status
Install Deck Shuttering	March 2026	Complete 
Install East Reinforcement	March 2026	Complete 
Install West Reinforcement	March 2026	Complete 
Deck Concrete Pouring (excl. curing time)	March 2026	Complete 

[Web Page Link](#)  
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

## Programme Updates Previous Month:

The progress against the planned activities from last month are as follows:

Activity	Completion Date	Status
Install Deck Formwork/Shuttering	March 2026	Complete 
Install Steel Reinforcement to Deck	March 2026	Complete 
Install Steel Deck Reinforcement (East)	March 2026	Complete 
Install Steel Deck Reinforcement (West)	March 2026	Complete 
Cast Deck Slab (Pour 1)	March 2026	Complete 
Cast Deck Slab (Pour 2)	March 2026	Complete 
Cast Deck Slab (Pour 3)	April 2026	Complete 
Cast Deck Slab (Pour 4)	April 2026	Complete 

\*Information is dated 08/04/2026

### [Web Page Link](#)

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

## Programme Updates Next Month:

The planned activities over the next month are:

Activity	Completion Date	Status
Spray Waterproofing	April 2026	Not Started
Install Sand Bed to Deck and Approaches	April 2026	Not Started
Install Bridge Deck Waterproofing	April 2026	Not Started
Install Back Fill to Approaches	April 2026	Not Started
Brick Parapet Buildup	May 2026	In-Progress
Parapet Concrete Infills	May 2026	Not Started
Parapet Copers	May 2026	Not Started
Cadent Gas Mobilisation	May 2026	In-Progress

[Web Page Link](#)

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

## Site Works - Look Ahead:

Our key upcoming works are:

2025				2026							
Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	
Key Activities							Completion Date		Status		
1	Traffic management installed. Site setup, including initial service diversions, service scaffold construction.						31/10/2025		Complete		
2	Service diversions complete, site layout finalised, demolish existing bridge (piers & abutments retained).						25/12/2025		Complete		
3	Reconstruction of bridge deck, parapet installation, deck reinforcement. Start of drainage and approach units.						22/03/2026		Complete		
4	Installation of ducting, kerbing, road lining, tarmac surface. Completion of road safety audits. Services re-diverted.						June 2026		Planned (On-target)		
5	Completion of final road safety audit, removal of traffic management, final services re-installed.						July 2026		Planned (On-target)		




[Web Page Link](#)

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

## March and April 2026 Progress Photos:

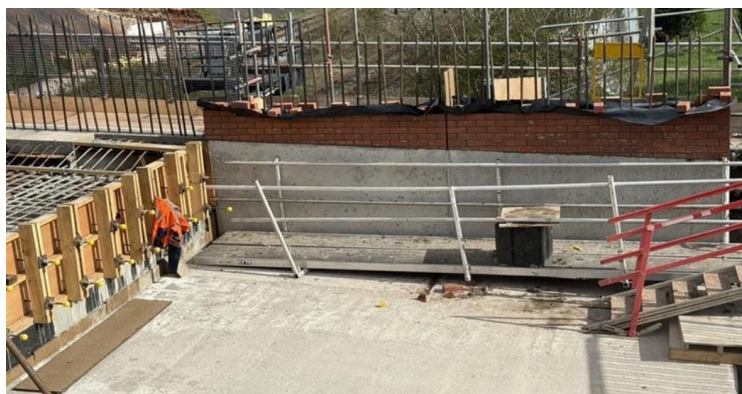

We've shared video of our recent work to lift the pre-cast bridge units into place on our web page [www.networkrail.co.uk/kirkhill](http://www.networkrail.co.uk/kirkhill) This work was completed earlier in March. We will continue with other work to complete the reconstruction over the coming months. Thank you to everyone in the community for their patience while we continue with this work.

[Web Page Link](#)

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

## Communications Updates - Parish Council and Nottinghamshire County Council Meeting:

Due to increased traffic on some roads since the closure of the A6006 in September 2025, Network Rail is formalising a one-off funding contribution to Nottinghamshire County Council (NCC). This funding is intended to be used on a number of local roads being used as unofficial diversions to help address increased road safety concerns, notably pothole repairs.

NR has held a number of collaborative discussions in the last 3 weeks with Via East Midlands (Via EM), and NCC to make this happen and we are targeting the end of March 2026 latest for the funding to be with NCC. A joint statement from NR, NCC and Via EM will be issued once finalised and there will be no further updates on this matter until then.

### Key Updates:

- Social value opportunities are currently being reviewed and will be reported in due course.
- Some of the site management team (both Network Rail and AMCO) completed litter picking along Leake Lane on Tuesday 10<sup>th</sup> March. Any further ideas for social value activities are welcomed by the project team.

[Web Page Link](#)

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

## Meetings Calendar:

Meeting dates between now and end of September are listed in the table below:

Month	Councillor Meeting
May	Wednesday 6 <sup>th</sup> May
June	Wednesday 3 <sup>rd</sup> June
July	Wednesday 1 <sup>st</sup> July Wednesday 29 <sup>th</sup> July
August	Wednesday 26 <sup>th</sup> August
September	Wednesday 23 <sup>rd</sup> September

The last councillor session was held on 8<sup>th</sup> April, with attendance/representation from:

### Nottinghamshire County Council:

Cllr Stuart Matthews  
Cllr John Cottee  
Cllr Bert Bingham  
Cllr Andy Brown

### Parish Councils:

Kegworth  
Normanton on Soar  
Stanford on Soar  
East Leake  
West Leake  
Rempstone  
Sutton Bonington

### Web Page Link

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.
