






Four Week Look Back:

Over the past month we have completed the following works, annotated on the image below.

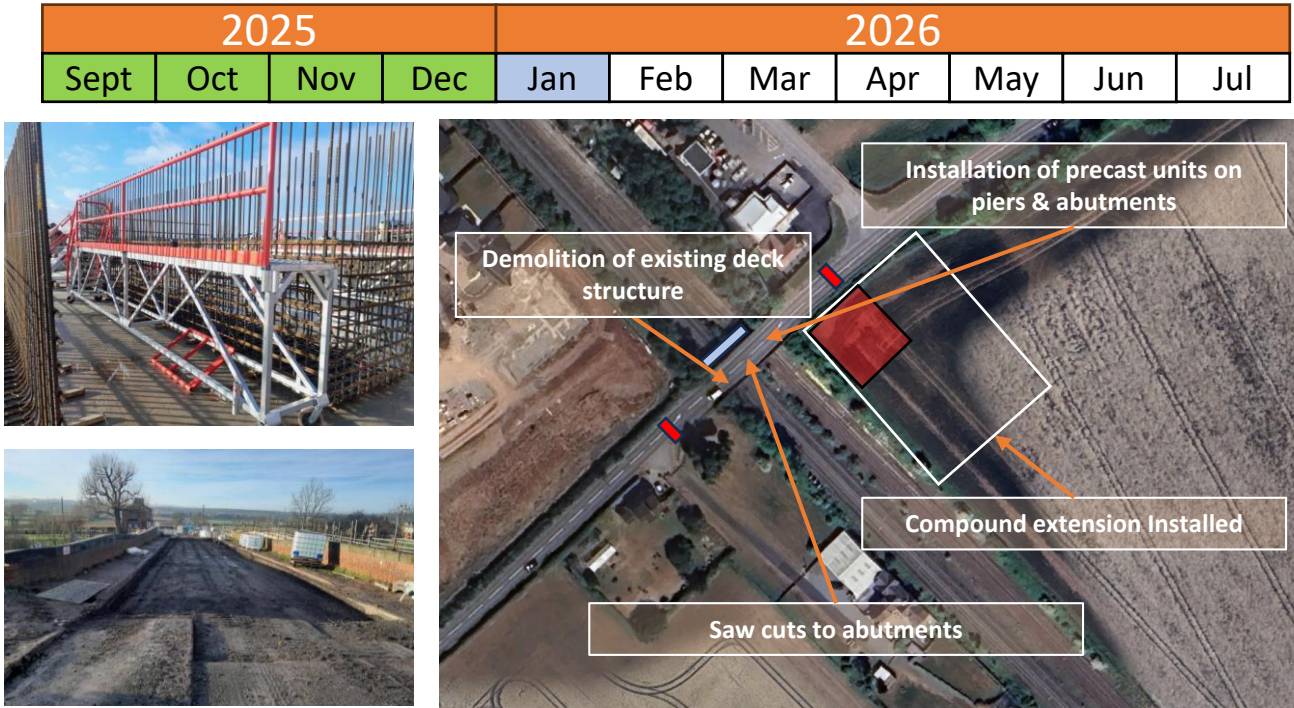








Activity	Completion Date	Status
Saw Cuts to Abutments	December 2025	Complete 
Compound Extension and Crane Pad Installation	December 2025	Complete 
Demolition of Existing Structure	December 2025	Complete 
Installation of Precast Concrete Units	December 2025	Complete 

[Web Page Link](#)
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

Programme Updates Previous Month:

The progress against the planned activities from last month are as follows:

Activity	Completion Date	Status
Abutment saw cuts	December 2025	Complete 
Central Pier saw cuts	December 2025	Complete 
Additional works to crane pad	December 2025	Complete 
Steel fixing for rebar cages	December 2025	Complete 
Remove existing bridge surfacing and copers	December 2025	Complete 
Mobilise demolition plant and materials	December 2025	Complete 
Crane delivery & rigging	December 2025	Complete 
Demolish spans and reduce central pier	December 2025	Complete 
Install precast units and rebar cages	December 2025	Complete 

*Information is dated 12/01/2026

[Web Page Link](#)
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

Programme Updates Next Month:

The planned activities over the next month are:

Activity	Completion Date	Status
Remove demolition spoil and plant	January 2026	In-Progress
Follow-up works (Re-profiling etc.)	January 2026	In-Progress
Compound Maintenance (Post-Demolition)	January 2026	Not Started
Concrete Pours to Pier/Abutments	February 2026	Not Started
Crane Delivery for Reconstruction	February 2026	Not Started
Install Additional Access Ramp	February 2026	Not Started

[Web Page Link](#)
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

Site Works - Look Ahead:

Our key upcoming works are:

2025				2026						
Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
	Key Activities			Completion Date			Status			
1	Traffic management installed. Site setup, including initial service diversions, service scaffold construction.			31/10/2025			Complete 			
2	Service diversions complete, site layout finalised, demolish existing bridge (piers & abutments retained).			25/12/2025			Complete 			
3	Reconstruction of bridge deck, parapet installation, deck reinforcement. Start of drainage and approach units.			22/03/2026			Planned (On-target)			
4	Installation of ducting, kerbing, road lining, tarmac surface. Completion of road safety audits. Services re-diverted.			June 2026			Planned (On-target)			
5	Completion of final road safety audit, removal of traffic management, final services re-installed.			July 2026			Planned (On-target)			



[Web Page Link](#)
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

Kirk Hill Bridge Project Monthly Newsletter (January 2026)



December 2025 Works:



[Web Page Link](#)
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

Traffic Management:

Our traffic management arrangements are shown on the website linked at the bottom of this page.

We aim to minimise any disruption to residents while the works are taking place and would like to remind you that the businesses on Hathernware industrial estate remain open throughout the works.

Local area flood plan has been completed in anticipation of possible adverse weather impacting current traffic management arrangements.

Traffic management was removed in response to the flood plan during the amber weather alert in the week of 10th November.

Community Engagement:

We have undertaken the following community engagement over the past month:

- Regular sessions with local councillors have been set up to provide updates and assurances over the works every 4 weeks.
- Follow-up session for neighbours immediately adjacent to the bridge was held on 26/11, presentation slides available on the Kirk Hill project website.



Web Page Link

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.
