


## Four Week Look Back:

Over the past month we have completed the following works, annotated on the image below.

2025				2026						
Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul

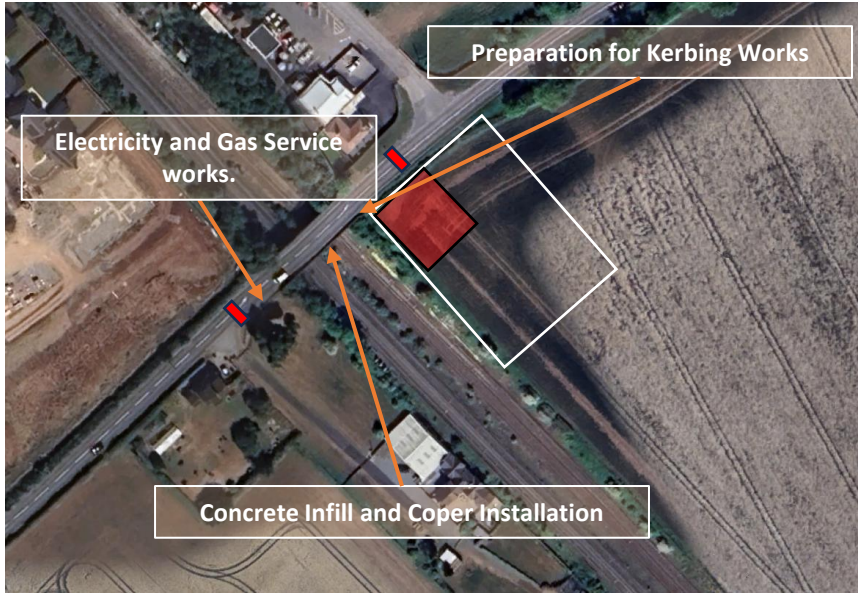

Activity	Completion Date	Status
National Grid and Cadent Service Reinstatement	May 2026	Complete 
Parapet Concrete Works	May 2026	Complete 
Install Parapet Copers	June 2026	Complete 
Trief (Anti vehicle incursion) Kerbing Preparation Works	June 2026	In-Progress

[Web Page Link](#)  
[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

## Programme Updates Previous Month:

The progress against the planned activities from last month are as follows:

Activity	Completion Date	Status
Parapet Concrete Infilling	May 2026	Complete 
Coper Installation and Jointing	May 2026	Complete 
New HV & LV Cables Changeover	May 2026	Complete 
New Cadent Gas Main Re-diverted Into Deck	May 2026	Complete 
New BT Openreach Cables Installed and transferred	June 2026	In-Progress
New Severn Trent Water Main Re-Diverted and transferred	June 2026	In-Progress
Kerb Installation	June 2026	In-Progress

\*Information is dated 11/06/2026

### [Web Page Link](#)

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

## Programme Updates Next Month:

The planned activities over the next month are:

Activity	Completion Date	Status
Transfer water supply to permanent service	June 2026	In-Progress
Trief Kerb (Anti Vehicle Incursion Kerbs) Steelwork**	June 2026	In-Progress
Trief Kerb Concrete Pours	June 2026	In-Progress
Remove Scaffold Bridge	June 2026	Not Started
Install Trief Kerbs	July 2026	Not Started
Install Bridge Surface Drainage	July 2026	Not Started
Road Sub-base and Footpath Installation	July 2026	Not Started
Tarmac Surfacing and Road Lining Installation	July 2026	Not Started
VRS Barrier Tie-in	July 2026	Not Started
Road Opens	July 2026	Not Started

\*\*Trief kerbs form part of the vehicle restraint system to prevent vehicles from falling onto the railway if an accident occurs.

### [Web Page Link](#)

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

## Site Works - Look Ahead:

Our key upcoming works are:

2025				2026						
Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
	Key Activities			Completion Date			Status			
1	Traffic management installed. Site setup, including initial service diversions, service scaffold construction.			31/10/2025			Complete 			
2	Service diversions complete, site layout finalised, demolish existing bridge (piers & abutments retained).			25/12/2025			Complete 			
3	Reconstruction of bridge deck, parapet installation, deck reinforcement. Start of drainage and approach units.			22/03/2026			Complete 			
4	Installation of ducting, kerbing, surface. Start of road safety audits. All services re-installed.			June 2026			In-Progress (On-target)			
5	Completion of final road safety audit, removal of traffic management, road lining, tarmac			July 2026			In-Progress (On-target)			



[Web Page Link](#)

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

## May and June 2026 Progress Photos:



Video showcasing the site works from our site team:

[Kirk Hill bridge project - Network Rail](#)

[Web Page Link](#)

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.

## Meetings Calendar:

Meeting dates between now and end of September are listed in the table below:

Month	Councillor Meeting
July	Wednesday 1 <sup>st</sup> July Wednesday 29 <sup>th</sup> July
August	Wednesday 26 <sup>th</sup> August
September	Wednesday 23 <sup>rd</sup> September

The last councillor session was held on 3<sup>rd</sup> June, with attendance/representation from:

### Nottinghamshire County Council:

Cllr Stuart Matthews  
Cllr John Cottee  
Cllr Bert Bingham  
Cllr Andy Brown

### Parish Councils:

Kegworth  
Normanton on Soar  
Stanford on Soar  
East Leake  
West Leake  
Rempstone  
Sutton Bonington

### Web Page Link

[Kirk Hill bridge project - Network Rail](#)

Get in touch with our 24-hour national helpline on 03457 11 41 41.
